

GOVERNANCE AND IMPLEMENTATION STRATEGY DOCUMENT



End-to-End Salesforce CRM Transformation for Customer Operations and Service Management

Authore : Mecek Kristina Br Sembiring

8.1 Governance Framework

Following the successful completion of Milestones 1 through 7, GreenGrid Utilities has implemented a comprehensive Salesforce CRM platform designed to improve customer service operations, field service coordination, automation, security, and executive reporting capabilities.

Milestone 1 established the business objectives and stakeholder requirements. Milestone 2 identified operational bottlenecks and process inefficiencies. Milestone 3 translated business requirements into a Salesforce solution architecture. Milestone 4 implemented the data model and custom objects. Milestone 5 introduced security controls and access management. Milestone 6 automated critical business processes using Salesforce Flows. Finally, Milestone 7 provided reporting and dashboard analytics for operational monitoring.

To ensure the long-term sustainability, security, and scalability of these implementations, GreenGrid Utilities establishes a formal governance framework. This framework provides oversight for platform administration, change management, security compliance, release management, and continuous improvement initiatives.

The governance model protects the investments made throughout the previous milestones while ensuring that future enhancements remain aligned with business goals and operational requirements.

8.1.1 Center of Excellence (CoE) Structure

To maintain effective platform governance, GreenGrid Utilities establishes a cross-functional Center of Excellence (CoE). The CoE is responsible for reviewing platform performance, evaluating enhancement requests, monitoring user adoption, and ensuring compliance with organizational policies.

Executive Sponsor (Executive Management Tier)

The Executive Sponsor provides strategic oversight and ensures that Salesforce initiatives continue to support the business objectives defined during Milestone 1. This role evaluates whether proposed improvements contribute to operational efficiency, service quality, and customer satisfaction goals.

Business Change Lead (Customer Support and Field Operations Management)

The Business Change Lead acts as the primary representative of end users. This role validates that proposed system changes accurately reflect operational processes established throughout Milestones 2, 4, and 6. The Business Change Lead also ensures that business requirements remain aligned with platform capabilities.

System Administrator (IT Governance Team)


The System Administrator serves as the primary custodian of the Salesforce environment. Responsibilities include managing user access, monitoring platform performance, maintaining security settings, supporting reports and dashboards, and overseeing automation components such as Flow 1 and Flow 2.

The System Administrator also coordinates deployment activities and ensures compliance with governance standards before any changes are introduced into production.

8.1.2 Environment and Release Management Strategy

As the Salesforce platform now supports critical business operations including customer case management, utility asset tracking, field technician dispatching, workflow automation, and executive reporting, a controlled release management strategy is required.

To satisfy the platform availability requirement defined in NFR1 (99.9% uptime), configuration changes must not be performed directly in the Production environment. Instead, all modifications follow a structured deployment process using multiple environments.

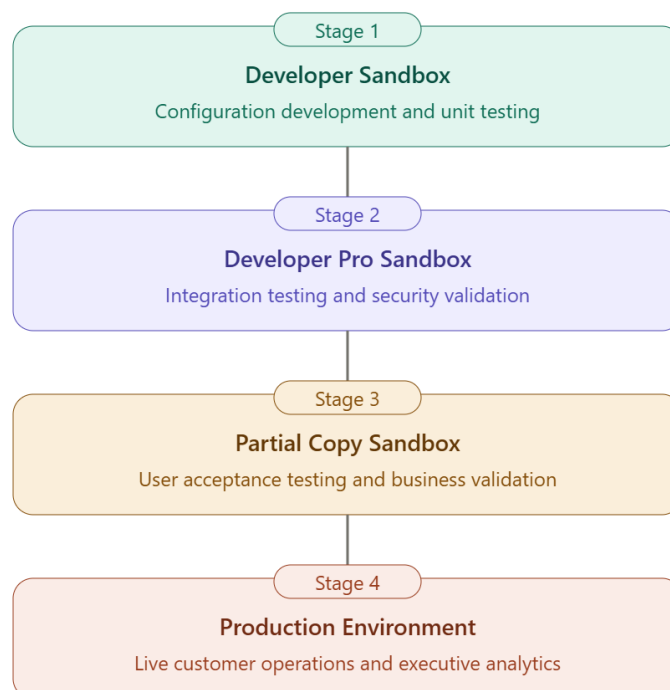

[Click any stage to learn more](#)

This release management approach minimizes operational risks by ensuring that all custom objects, security configurations, automation flows, reports, and dashboards are fully validated before deployment.

The strategy also supports future enhancements without disrupting daily business operations.

8.1.3 Change Control Board (CCB) Protocols

Because the Salesforce environment now contains critical business processes developed throughout Milestones 4, 5, 6, and 7, any significant modification must pass a formal Change Control Board (CCB) review before deployment.

The CCB evaluates all requests affecting custom objects, security settings, workflow automations, reports, dashboards, and data management processes.

Risk Assessment

The proposed change must be reviewed to determine whether it impacts operational performance targets, including the high-speed Meter ID lookup requirement defined in FR1 and other critical business functions.

Security Assessment

The modification must be assessed to ensure continued compliance with the Private Organization-Wide Default (OWD) model, role hierarchy configuration, permission assignments, and sharing settings established in Milestone 5.

Rollback Planning

Before deployment approval is granted, administrators must prepare a rollback procedure that enables the organization to restore the previous configuration state within a fifteen-minute recovery window should unexpected production issues occur.

This process minimizes business disruption and protects operational continuity.

8.2 User Adoption Strategy

Although the technical implementation of the Salesforce CRM platform was completed through Milestones 4 to 7, the long-term success of the project depends heavily on user adoption.

GreenGrid Utilities therefore implements a structured adoption strategy designed to support employees during the transition from spreadsheet-based processes to a centralized CRM environment. The objective is to reduce resistance to change, improve user confidence, and eliminate the operational inefficiencies identified in Milestone 2.

8.2.1 Role-Based Training Programs

Training activities are customized according to the responsibilities and system interactions of each user group.

Customer Support Training Program

Customer Support Agents receive hands-on training focused on the Salesforce Service Console environment.

Training activities include:

- Managing customer service interactions.
- Performing Meter ID searches.
- Creating and updating Case records.
- Assigning priority levels.
- Managing outage incidents.
- Triggering automated dispatch activities through Flow 1.

Practical simulation exercises are used to familiarize agents with real operational scenarios.

Field Operations Training Program

Field Technicians participate in mobile-focused training sessions using the Salesforce Mobile Application.

Training activities include:

- Accessing assigned field visits.
- Receiving real-time dispatch notifications.
- Updating repair progress.
- Changing Repair_Status__c to Resolved.
- Entering Technician_Notes__c.
- Synchronizing field data through Flow 2.

The training program ensures that technicians can perform all required activities without relying on manual paperwork.

8.2.2 Adoption Metrics and Performance Monitoring

To measure implementation success, GreenGrid Utilities monitors user adoption through Salesforce reporting and analytics tools.

Three key performance indicators are used:

Login Frequency

Measures whether Customer Support Agents and Field Technicians actively access Salesforce on a daily basis.

The objective is to achieve full user participation across all operational teams.

Data Completeness Rate

Evaluates the quality of data entered into the system.

Closed cases are reviewed to ensure that Technician Notes, repair updates, and customer service records are completed accurately without missing information.

Dashboard Engagement

Tracks how frequently management personnel access the Executive Operations Dashboard developed during Milestone 7.

This metric helps determine whether organizational decisions are being supported by data-driven insights generated through Salesforce analytics.

8.3 Implementation Plan

The implementation plan represents the final phase of the Salesforce CRM transformation project initiated in Milestone 1 and progressively developed through Milestones 2 to 7.

A phased deployment approach is adopted to minimize operational disruption while ensuring adequate time for testing, validation, training, and support activities

Stage A: Environment Preparation and Security Baseline (Weeks 1–2)

During this phase, foundational platform components are prepared and validated.

Key activities include:

- Establishing metadata structures.
- Configuring custom objects.
- Implementing Private OWD settings.
- Creating the Role Hierarchy.
- Validating Profiles and Permission Sets.
- Preparing sandbox environments.

The objective is to establish a secure and stable foundation for subsequent implementation activities.

Stage B: Data Migration and Automation Deployment (Weeks 3–4)

This phase focuses on migrating operational data and implementing automated business processes.

Key activities include:

- Importing customer records from spreadsheet sources.
- Migrating Utility Asset information.

- Validating Meter ID indexing.
- Performing duplicate detection and data cleansing.
- Deploying Flow 1 (Automated Field Dispatch Trigger).
- Deploying Flow 2 (Real-Time Operational Sync and Case Closure).

Successful completion of this stage ensures that the organization can begin operating within the Salesforce environment.

Stage C: User Training, Go-Live, and Hypercare Support (Weeks 5–6)

The final implementation phase focuses on user readiness and production deployment.

Key activities include:

- Conducting role-based training programs.
- Deploying validated configurations into Production.
- Executing smoke testing procedures.
- Monitoring system performance.
- Providing Hypercare support during the initial production period.

During Hypercare, dedicated support resources remain available to resolve issues quickly and ensure a smooth transition into live operations.

Conclusion

With the completion of Milestone 8: Governance and Implementation Strategy, the Salesforce CRM transformation project at GreenGrid Utilities reaches its final phase.

Beginning with business analysis and stakeholder identification in Milestone 1, continuing through process assessment, solution architecture design, data modeling, security configuration, workflow automation, reporting, and analytics development in Milestones 2 through 7, the organization has successfully established a fully integrated customer operations and field service management platform.

The governance framework introduced in this milestone ensures that all previous implementations remain secure, scalable, and sustainable after deployment. Through structured governance procedures, change management controls, user adoption initiatives, and phased implementation planning, GreenGrid Utilities is positioned to maximize the long-term value of its Salesforce investment.

The completed Salesforce solution provides a unified environment for customer service operations, field technician coordination, automation management, executive reporting, and strategic decision-making, ultimately achieving the business objectives defined at the start of the transformation initiative.
